

# Harrison Elem. Weekly Blitz: June 19<sup>th</sup>, 2020





**Harrison Elementary:** The indoor air-handling units have been delivered and set into place. In Area B, the 2nd floor bearing walls have reached the roof level and the roof steel has been set. The interior wall framing at the 1<sup>st</sup> floor is nearly complete and the 2<sup>nd</sup> floor is starting layout. In-wall and above ceiling MEP rough-in continues in both Areas.



# Crosby Elem. Weekly Blitz: June 19<sup>th</sup>, 2020



**Crosby Elementary:** In Area A, the stage bearing walls continue to rise and the mezzanine concrete floor has been poured. The steel joists in the gym are being detailed in preparation for roof decking. In Area B, the 1<sup>st</sup> floor interior walls and door frames are being framed and set. In-wall and above ceiling MEP rough-in continues in both Areas.

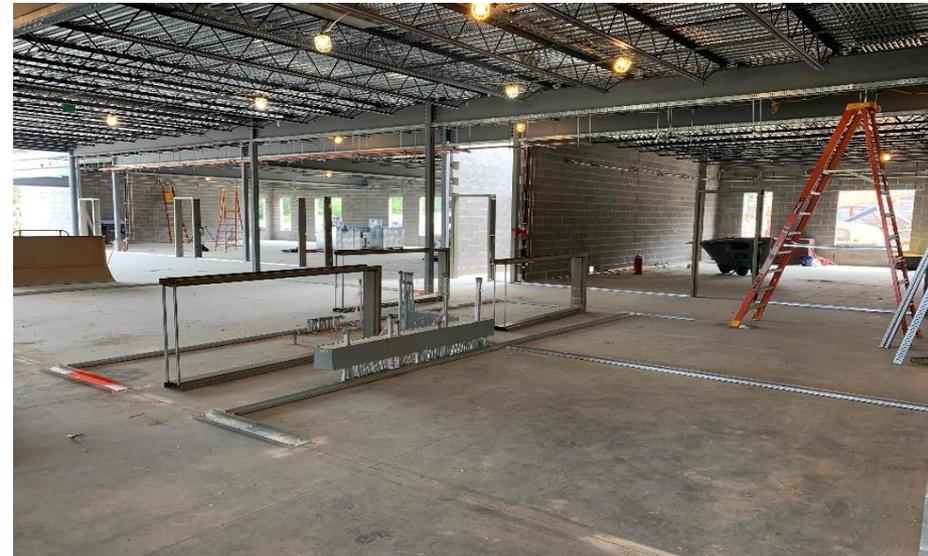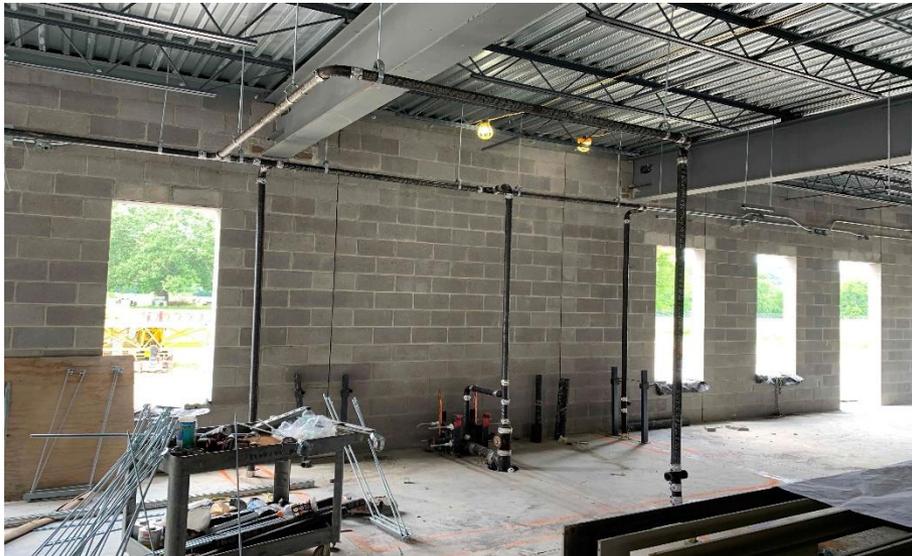

# Miami Whitewater Weekly Blitz: June 19<sup>th</sup>, 2020



**Miami Whitewater Elementary:** The gym bearing walls continue to rise in Area A. In Area B, metal stairs have been installed up to the 2<sup>nd</sup> floor and layout has begun for the 1<sup>st</sup> floor interior walls. The North half of the 2<sup>nd</sup> floor steel is being set. In-wall and above ceiling MEP rough-in continues in both Areas.



# Junior High Weekly Blitz: June 19<sup>th</sup>, 2020



**Harrison Junior High:** Structural steel is being set in the West half of the academic wing and bearing block walls are rising in Area B. In Area C, the gym, kitchen, and locker room concrete floors were poured and the admin area is being prepped for next week's concrete pour. In-wall and above ceiling MEP rough-in continues.





