


Harrison Elem. Weekly Blitz: September 18th, 2020



Harrison Elementary: In Area A, the interior walls are being framed in the art room and administration area while the roof is being installed overhead. In the Area B academic wing, the 2nd floor's drywall is being finished and painted. Brick is being laid in the courtyard and on the South wall of Area B. Above ceiling MEP rough-in continues in both Areas.

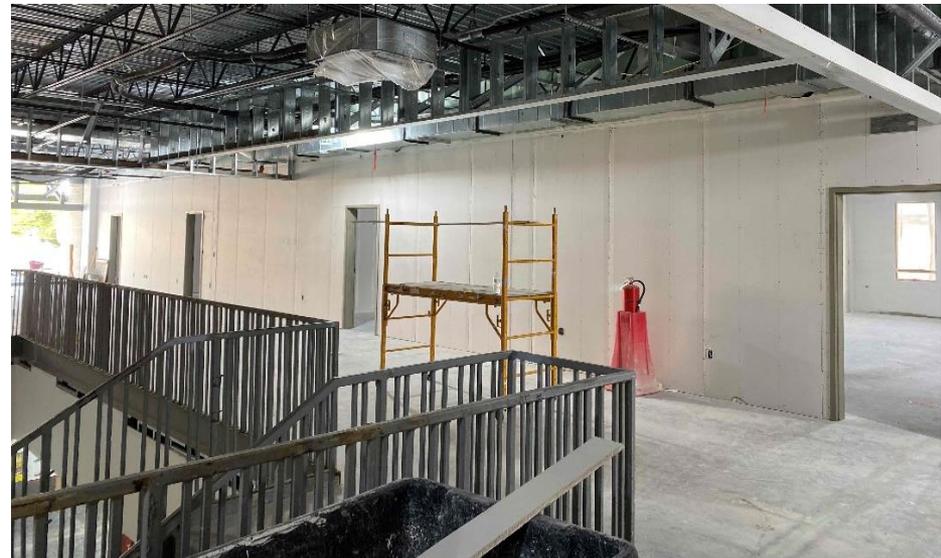

Crosby Elem. Weekly Blitz: September 18th, 2020




Crosby Elementary: In Area B, drywall is being hung on the 1st floor and interior CMU block walls are being laid around the restrooms on the 2nd floor. In Area A, the kitchen roof is being installed and steel is being erected in the administration area. Brick is being laid on the North and East wall of Area B. In-wall and above ceiling MEP rough-in continues in both Areas.



Miami Whitewater Weekly Blitz: September 18th, 2020



Miami Whitewater Elementary: Metal roof decking is being installed in the kitchen, mechanical, administration, and art room. In Area B, roof installation continues as the interior walls on the 2nd floor are being laid out and framed. Brick has begun on the East wall of Area B. Above ceiling MEP rough-in continues in both Areas.

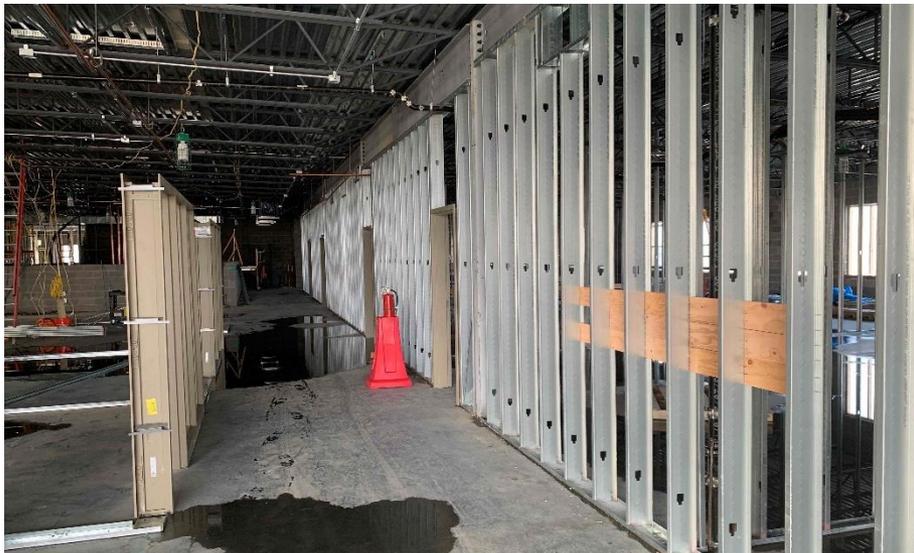


Junior High Weekly Blitz: September 18th, 2020



Harrison Junior High: Interior walls on level 2 of Area A and level 1 of Area B are being laid out and framed. Bearing block walls continue to rise in all three Areas while roof steel is being set on the 2nd floor of Area B. The concrete seating for outdoor classes has been poured in the courtyard. In-wall and above ceiling MEP rough-in continues in all Areas.



Elementary School Floor Plans

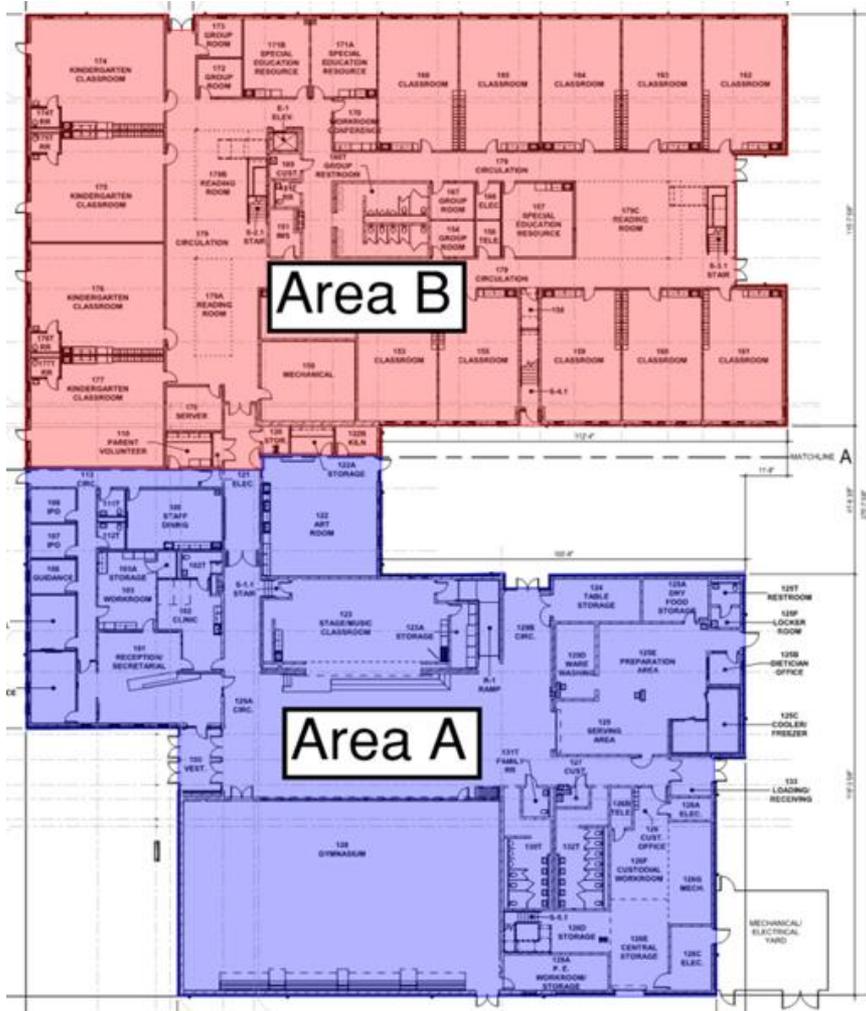

Junior High School Floor Plans

